# Lab 2: Agile Backlog Creation & Sprint Simulation in Jira

**Name: Akanksha.P**


**SRN: PES1UG25CS801**

**Objective:**


Using Jira to turn functional requirements into Agile backlog items, simulate a sprint, and analyse progress.

**Deliverables:**


- **Jira backlog with Epics and User Stories.**

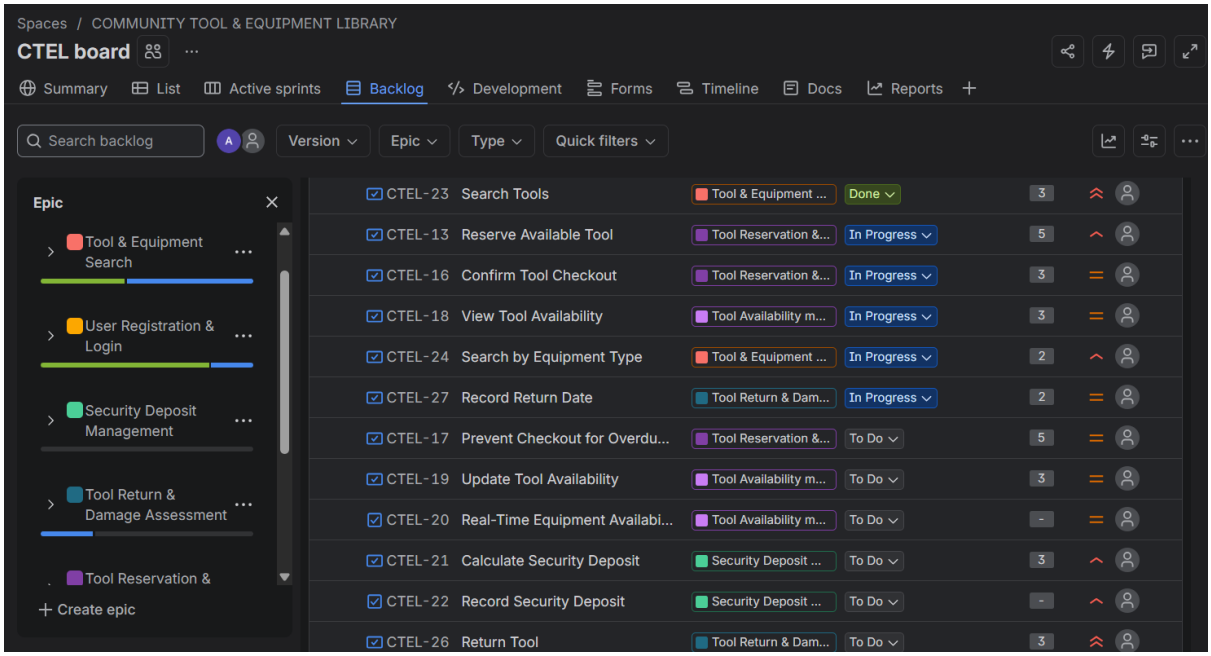


- **Story point assignments.**

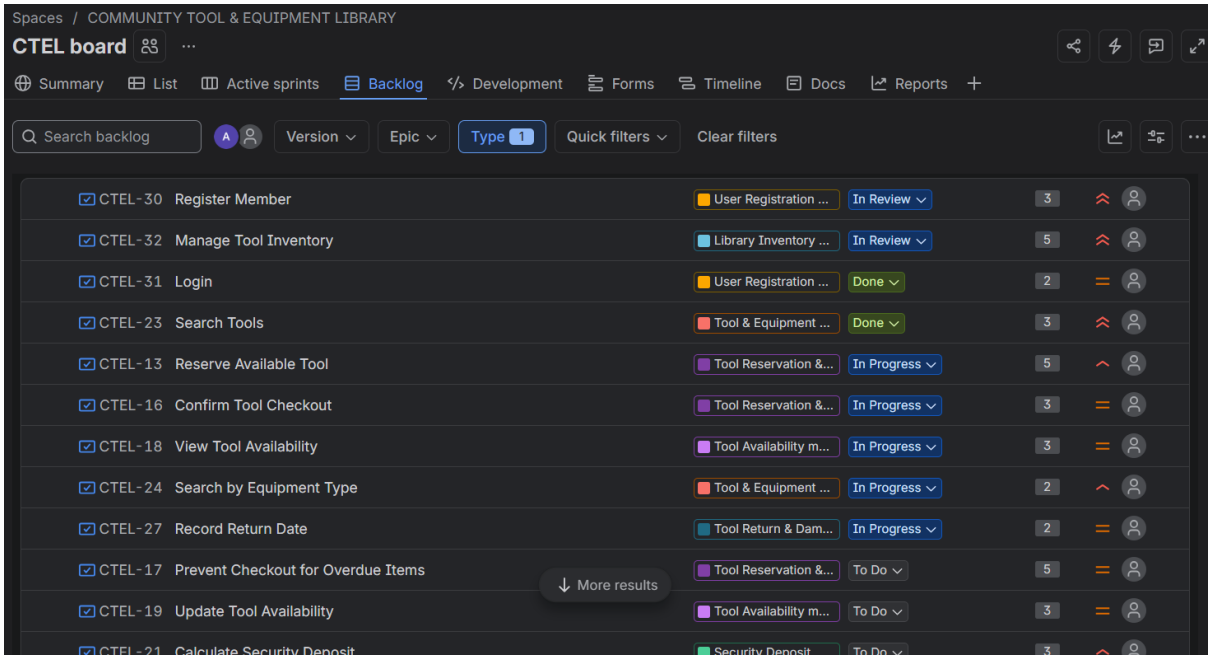


- **Sprint board (Active Sprint view).**

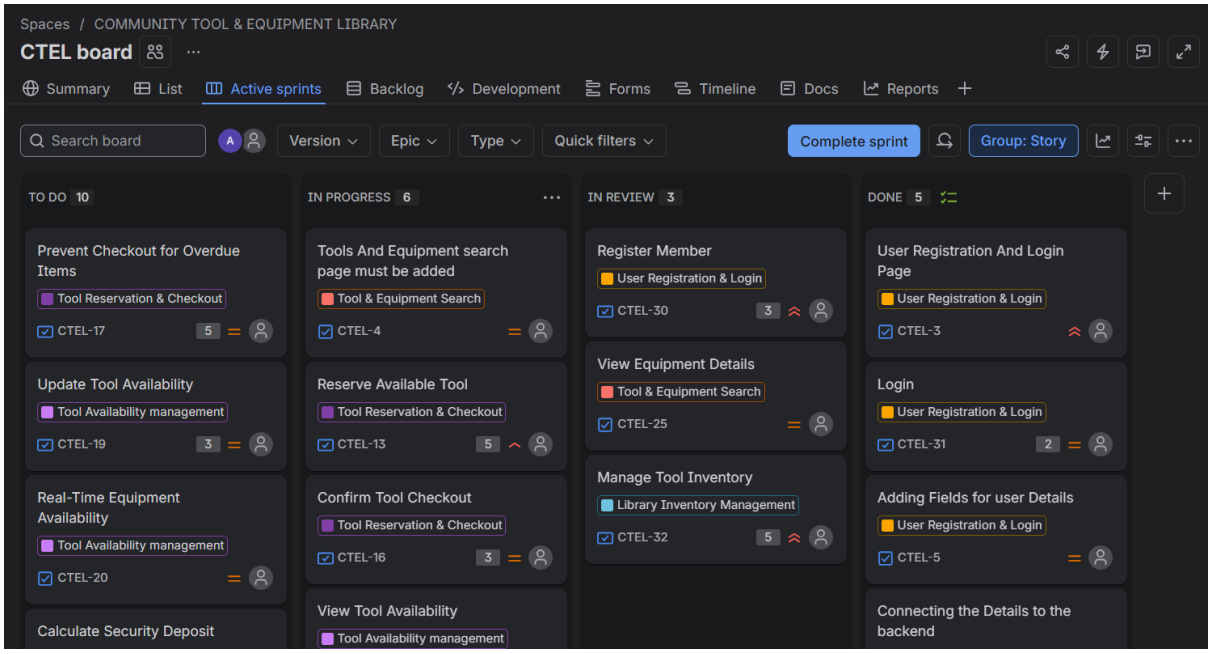

- **Burndown Chart.**

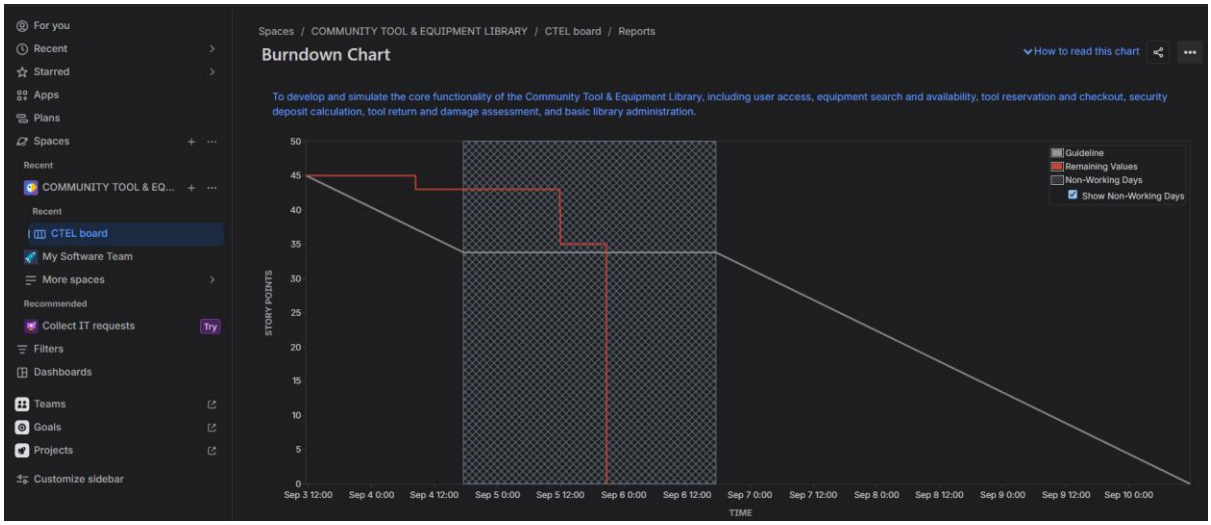


## Reflection Questions:

1. **Did your estimations reflect the actual effort?**
   Yes, the story point estimations were mostly close to the actual effort required for the tasks. Smaller and simpler stories, such as login and viewing equipment details, were given fewer points, while more complex stories like tool reservation, real-time availability and checkout were given higher points. This helped me understand the effort and complexity involved in each user story.

2. **Was your backlog well-prioritized?**
   Yes, I prioritized the backlog based on the importance of each feature to the users and the overall system. Core functionalities such as tool availability, searching, reservation, checkout and security deposit calculation were given higher priority because they are important for the main purpose of the system. Features related to administration and management were given lower priority.

3. **How did your simulated sprint align with your plan?**
   The simulated sprint followed the plan that I created during sprint planning. I selected the required user stories from the backlog and moved them through To Do, In Progress and Done based on their progress. The sprint mainly focused on completing the important functionalities of the Community Tool & Equipment Library. Overall, the sprint helped me understand how planned backlog items are executed within a fixed time period.

4. **What insights did the burndown chart give about your team's capacity?**
   The burndown chart helped me understand how much work was completed and how much work was still remaining during the sprint. As the user stories were moved towards completion, the remaining story points decreased. It also helped me compare the actual progress with the expected progress and understand whether the amount of work planned for the sprint was manageable for the team
